# **ROUTE 16 CONSTRUCTION SUMMARY REPORT**

WEDNESDAY, MAY 31, 2017 BERLIN, NEW HAMPSHIRE

BUSINESSES

**ARE OPEN** 

# PATIENCE PLEASE... It will be worth it!

#### ANTICIPATED CONSTRUCTION PHASING

- **Phase I** Mill and Overlay (Twelfth St. north)
- **Phase II** Full Reconstruction (Seventh Eighth St. and Twelfth St. intersection)
- **Phase III** Full Reconstruction (St. Anne's Church to Twelfth St. intersection, excluding Phase II area)


## **WORK PROGRESS (Last 2 Weeks)**

- **Phase I** Complete.
- **Phase II** No work scheduled until June 15, 2017.
- **Phase III** Ongoing
  - Removed old and installed new drainage from Ninth Street to Eleventh Street.
  - Overhead utility reconstruction continues to progress. St. Anne's Church to Eternal Machines is complete; nearly complete up to Seventh St.

# **WORK SCHEDULED (Next 2 Weeks)**

#### Phase III

- Drainage installations are moving toward completion between Eighth St. and Twelfth St.
- Drainage installations will begin between Iceland St. and Viking St.
- Loaming and seeding will continue along northbound lane between Cambridge St. & Maple St.
- Sidewalk construction will begin, starting near Northern Lights and moving north.

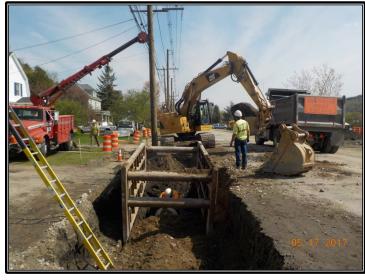

### MAINTENANCE OF TRAFFIC

The southbound detour will continue from Twelfth St. to Eighth St. until drainage installations are complete. This detour will also be utilized during box-cutting of the road to prepare for new gravels and pavement.

Please note, on-street parking spaces will likely be utilized by construction equipment during sidewalk construction starting near Northern Lights and moving north.

Thank you for your continued patience!

If you would like to receive this document by email, please contact Pam LaFlamme at plaflamme@berlinnh.gov



City of Berlin • www.berlinnh.gov 168 Main Street Berlin, NH 03570 (603) 752-7532

